



Cultural Council

OF GREATER JACKSONVILLE

**MORE** ART.  
CULTURE.  
PLACES.

# Art in Public Places Committee

## Project Report

October 12, 2022

# Current & Upcoming Public Art Projects

## **Publicly-Funded Projects (APP Trust Fund .75% CIP Ordinanced dollars):**

1. Courthouse Plaza
2. Mandarin Parks
3. Southside Center
4. Duval County Public Schools Murals (*upcoming*)
5. Oceanway Library (*upcoming*)

## **Publicly-Funded Projects (Other Public Dollars):**

1. San Marco Intersection
2. King-Soutel Crossing CRA Plan Public Art (Office of Economic Development)
3. Vystar Veterans Memorial Arena Sculpture (MAVA & Vystar)
4. Don't Miss A Beat Murals
5. Roosevelt-Edgewood Underpass
6. City Council Chambers Art on Loan

# Current & Upcoming Private-Public Art Projects

## **Privately-Funded Projects:**

1. FIS Headquarters
2. Jacksonville Jaguars Miller Electric Center Project
3. Johnson Brothers Sculpture at Lift Ev'ry Voice and Sing Park
4. JTA

# PUBLICLY-FUNDED PROJECTS

# Courthouse Plaza Public Art

Project Manager(s): Michele Lee

Selected Artist: Cliff Garten

Budget: \$799,636; Art - \$687,663, Admin - \$72,861, Maint. - \$39,111



# CURRENT TIMELINE

**Nov.' 21 - August 2022**

**Contract Negotiations**

**August 23, 2022**

**ASP Meeting to Approve Final Design**

**November '22 - October '23**

**Fabrication + Installation**

**Nov. - December 2023**

**Dedication Ceremony`**

# Mandarin Parks Interactive Public Art: Losco Park

Project Manager(s): Ashley Wolfe (Lead) & Ailsing Millar McDonald

Selected Artist: Solomon Bassoff



# CURRENT TIMELINE

**June - August 2022**

**Procurement Processing**

**August - September 2022**

**Contracting**

**September - December 2022**  
**November 14, 2022**

**Artist(s) Design Phase**  
**\*Artist Visit to Jax**

**January - April '23**

**Fabrication + Installation**

**April 2023**

**Dedication Ceremony**



# Mandarin Parks Interactive Public Art: Rogers Park

Selected Artist: Greg Mueller



Chuck  
Rogers  
Park



# CURRENT TIMELINE

**June - August 2022**

**Procurement Processing**

**August 2022**

**Contracting**

**September - October 2022**

**Artist(s) Design Phase**

**September 6 - 7, 2022**

**\*Artist Visit to Jax**

**November - March '23**

**Fabrication + Installation**

**March - April 2023**

**Dedication Ceremony**

# Southside Senior Center Public Art

Project Manager(s): Ailsing Millar McDonald (Lead), Ashley Wolfe






# Southside Senior Center Public Art



# PUBLICLY-FUNDED PROJECTS (OTHER)

# San Marco Intersection Public Art

Project Manager(s): Ashley Wolfe

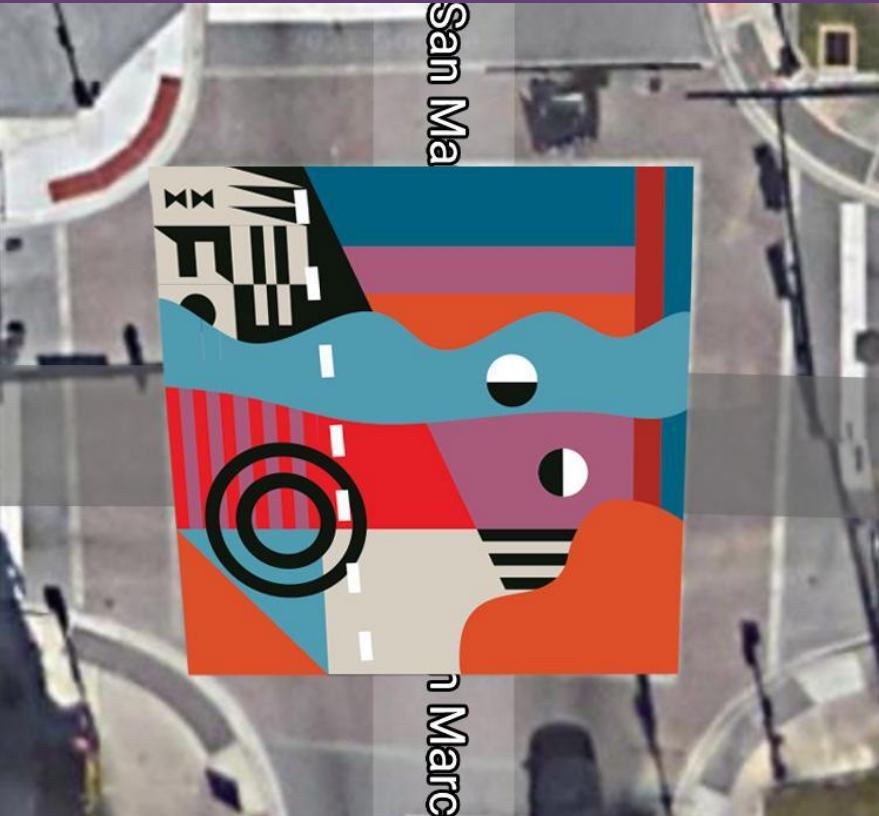

**June - August 2022**

**Bid Services through COJ  
Procurement**

**August - October 2022**

**Contracting + Permitting Phase**

**October - Nov., 2022**

**Artist Design Application + Installation**

**December - Jan. 2023**

**Dedication Ceremony**

# Vystar Veterans Memorial Arena Public Art

Project Manager(s): TBD



# PRIVATELY-FUNDED PROJECTS



# FIS, Sculpture 1 of 3

## Location A


Project Manager: Jen Jones Murray

Selected Artist: Ai Qui, Humanity Memorial Arts

Humanity Award Public Art Team, WV score 34

A

Install 1<sup>st</sup>  
Quarter 2023

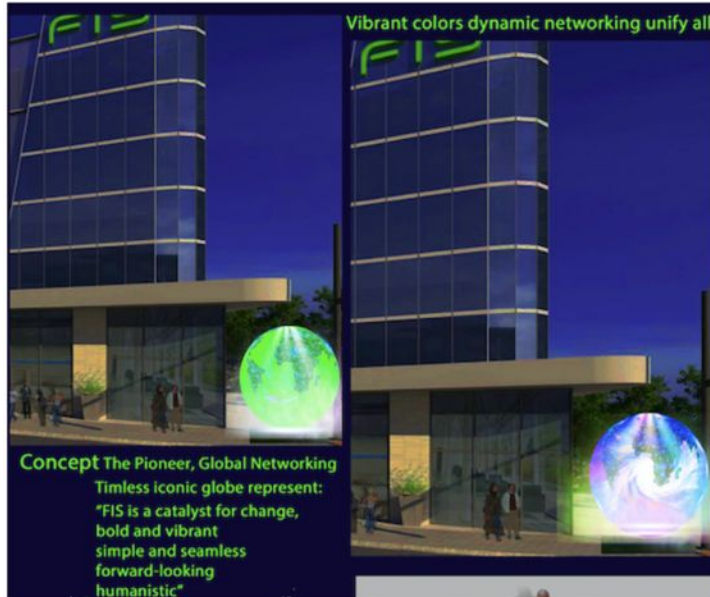

Humanity Memorial  
Stainless steel with copper finish

# FIS, Sculpture 2 of 3

Project Manager: Jen Jones Murray


Selected Artist: Sheila Wyne

## Location B

Sheila Wyne, AK\*

Install 1<sup>st</sup>  
Quarter 2023

The Walker  
Aluminum, repurposed street signs

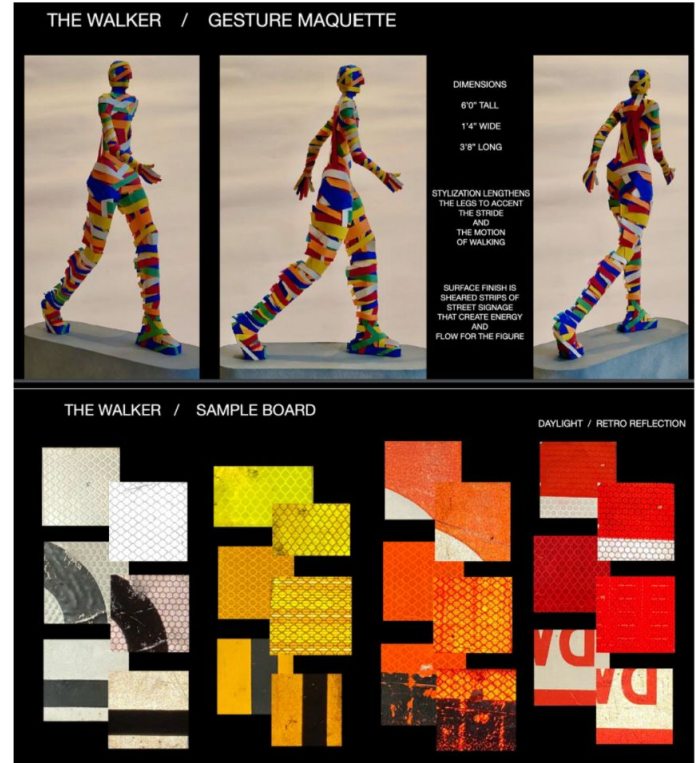

# FIS, Sculpture 3 of 3

## Location C

Project Manager: Jen Jones Murray

Selected Artist: Don Gialanella

Donald Gialanella, FL\*

score 38

A

Install 4<sup>th</sup>  
Quarter 2022



Cynosure  
Stainless Steel

# Jacksonville Jaguars, new Sports Performance Center

Project Manager: Jen Jones Murray

Selected Artists: To be determined, CTA's executing now






# Jacksonville Jaguars, new Sports Performance Center

## FIELD HOUSE NORTH AND WEST FACADES

Major  
Mural:  
Digital Art  
Printed to  
3M Vinyl

All  
Installs  
June  
2023

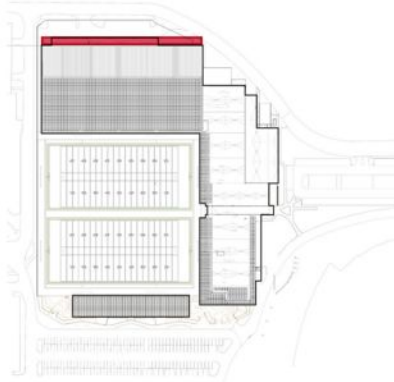

DOWNTOWN JACKSONVILLE MURAL



ART REPUBLIC, DOWNTOWN JACKSONVILLE MURAL



TAMPA BUCS MURAL, ST. PETERSBURG



WYNWOOD WALLS, MIAMI



"FIRST TEAM", DOWNTOWN JACKSONVILLE

# Jacksonville Jaguars, new Sports Performance Center

1 of 2  
Sculpture  
Gardens

Artfully  
created bike  
racks &  
large 3D  
works to be  
included



# Jacksonville Jaguars

**Categorized by the primary steps utilized to procure public art, here is our overall project management schedule for each of the artworks in the Jaguars project's forthcoming public art inventory.**

## Incoming Public Art Inventory

Qty. 2, impressive, sculptural, artistic bike racks

Qty. 1-2, freestanding sculptural works (actual qty finalized after major mural bid comes in to us in late August)

Qty 1, major work "Hoy es Hoy"

Qty 1, major vinyl mural

Qty 4, additional mid-smaller sized vinyl murals

Qty 12-20 works in Rotating Art Gallery Exhibit

## Installation Period

MAY 16 - JUNE 15, 2023

## Calls to Artist (CTA) RFP Drafts to be Submitted to Jags for Review

AUGUST 3, 2022: Qty. 2, impressive, sculptural, artistic bike racks

SEPTEMBER 2, 2022: Qty. 1-2, freestanding sculptural works (actual qty finalized after major mural bid comes in to us in late August)

COMPLETE: Qty 1, major work "Hoy es Hoy"

SEPTEMBER 2, 2022: Qty 1, major vinyl mural

SEPTEMBER 2, 2022: Qty 4, additional mid-smaller sized vinyl murals

JANUARY 6, 2023: Qty 12-20 works in Rotating Art Gallery Exhibit (exact quantity tbd after space is built, developing this portion of the project has a much lesser timeline)

# Jacksonville Jaguars

## Period Calls to Artist (CTA) RFP/RFQ Available for Responses by National, Regional, and Jacksonville Artists

AUGUST 15 - SEPTEMBER 30, 2022: Qty. 2, impressive, sculptural, artistic bike racks - RFPs

SEPTEMBER 15 - OCTOBER 31, 2022: Qty. 1-2, freestanding sculptural works (actual qty finalized after major mural bid comes in to us in late August) - RFPs

COMPLETE: Qty 1, major work "Hoy es Hoy"

SEPTEMBER 15 - OCTOBER 31, 2022: Qty 1, major vinyl mural - RFQ

SEPTEMBER 15 - OCTOBER 31, 2022: Qty 4, additional mid-smaller sized vinyl murals - RFQs

FEBRUARY 1 - MARCH 1, 2023: Qty 12-20 works in Rotating Art Gallery Exhibit

## Client Review & Selection Period for Each Artwork (RFPs) / Artist (RFQs)

OCTOBER 5 - 19, 2022: Select Artworks from Submitted Proposals - Qty. 2, impressive, sculptural, artistic bike racks - RFPs

NOVEMBER 8 - 22, 2022: Select Artworks from Submitted Proposals - Qty. 1-2, freestanding sculptural works (actual qty finalized after major mural bid comes in to us in late August) - RFPs

COMPLETE: Qty 1, major work "Hoy es Hoy"

NOVEMBER 8 - 22, 2022: Select Artist from Submitted Proposals - Qty 1, major vinyl mural - RFQ

NOVEMBER 8 - 22, 2022: Select Artist from Submitted Proposals - Qty 4, additional mid-smaller sized vinyl murals - RFQs

MARCH 10 - MARCH 28, 2023: Will have Delivered Our Draft (Ideal) Curatorial Plan Based Upon Submissions of Qty 12-20 works in Rotating Art Gallery Exhibit

## Design (RFQs only). Fabrication (RFPs only) & Installation Dates for Each Artwork

FABRICATION START DECEMBER 1, 2022 - INSTALLATION JUNE 1, 2023: Qty. 2, impressive, sculptural, artistic bike racks

FABRICATION START DECEMBER 1, 2022 - INSTALLATION JUNE 1, 2023: Qty. 1-2, freestanding sculptural works (actual qty finalized after major mural bid comes in to us in late August)

CLEANING, SEALING & RE-CRATING ON OCTOBER 5 - INSTALL MAY 17, 2023: Qty 1, major work "Hoy es Hoy"

DESIGN PERIOD DECEMBER 1 - FEBRUARY 1, 2023 & INSTALLATION MAY 16 - JUNE 15, 2023: Qty 1, major vinyl mural

DESIGN PERIOD DECEMBER 1 - FEBRUARY 1, 2023 & INSTALLATION MAY 16 - JUNE 15, 2023: Qty 4, additional mid-smaller sized vinyl murals

INSTALLATION JUNE 8, 2023: Qty 12-20 works in Rotating Art Gallery Exhibit



# REI Mural at Markets at Town Center

Project Manager(s): Jordan Stallings (Lead) & Ashley Wolfe



**Postponed to March 2023**

# THANK YOU!

For your service in choosing public art  
in our community.

**Contact us:**

Michele D. Lee, Interim Director of Public Art, [Michele@culturalcouncil.org](mailto:Michele@culturalcouncil.org)

Kat Wright, Assistant Director of Public Art, [Kat@culturalcouncil.org](mailto:Kat@culturalcouncil.org)

Ashley Wolfe, Public Art Project Manager, [Ashley@culturalcouncil.org](mailto:Ashley@culturalcouncil.org)

Iris Benson, Operations Coordinator, [Iris@culturalcouncil.org](mailto:Iris@culturalcouncil.org)
